



Project Update

Foxconn's Industrial Construction Work in Area 1
of Wisconn Valley Science & Technology Park

October 2019



Status Update

- Site Development continues as planned - cut/fill, building pad preparation, and storm water management.
- Site utility (sanitary / water) and roadway work is proceeding as planned.
- Roadway paving is underway.
- Fab – Precast complete, steel work is well underway, the concrete roof pours and under slab utilities have started.
- PSS - precast underway, screen wall construction continuing.
- Landscaping in the NE has begun



Next Steps and Procurement

FAB Foundations, Elevators, Testing

Power Substation

FAB Building Enclosure, Additional Site Work

Building Interiors

FAB MEP – Initial Phase

FAB Turnkey Systems, additional MEP Systems

Awarded

Awarded

Awarded

In Process

In Process

3rd-4th Quarters 2019



Wisconsin First and Racine County Economic Inclusion & Diversity Results to Date


Business Contracting and Inclusion Goals

Wisconsin based Businesses	60%
Racine County based Businesses	10%
Minority-Owned (MBE) Business Enterprises	10% Combined
Woman-Owned (WBE) Enterprises	
Veteran-Owned Business Enterprises	

Workforce Inclusion and Diversity Goals

Wisconsin Resident Work Hours with an emphasis on Racine County Residents	70%
Minorities or People of Color*	10% Combined
Women	
Veterans	

WISCONSIN FIRST Business Inclusion (as of 06/30/2019*) Work Orders 1,2,3a-b,4a

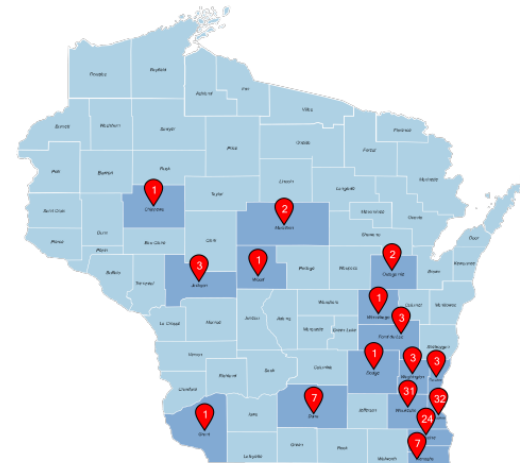


WISCONSIN
IMPACT

122
COMPANIES

96%
CONTRACT
VALUE

WISCONSIN FIRST Resident Inclusion (as of 06/30/2019*) Work Orders 1,2,3a-b,4a

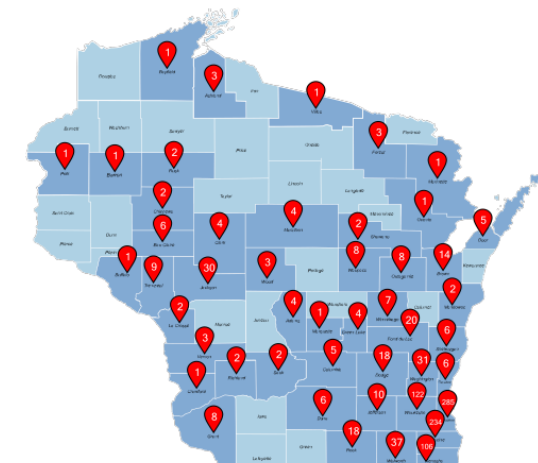

WISCONSIN
IMPACT

1051
RESIDENTS


96%
RESIDENT
PARTICIPATION

Gilbane|Exyte will deploy best efforts through robust outreach, procurement and construction practices to achieve the goals for the construction projects awarded for their work in the Science and Technology Park.

Stay Informed

Wisconnvalley.wi.gov

Primary site for contractors to engage with public infrastructure and building construction.



Site Photos



Site Photos



Site Photos



Site Photos

